Rocky Mountain Chocolate Factory - Aspen, Colorado
Sarrett Development Corporation

ID	Task Name	Duration	Start
1	Building permit	1 day	Wed 10/15/03
2	Demolition	3 days	Wed 10/15/03
3	Rough Framing	1 day	Mon 10/20/03
4	Rough Plumbing	4 days	Tue 10/21/03
5	Rough Electric	3 days	Tue 10/21/03
6	Rough HVAC	2 days	Thu 10/23/03
7	Rough inspection	0 days	Fri 10/24/03
8	Drywall Install Upstairs	1 day	Mon 10/27/03
9	Repair dywall in basement	2 days	Mon 10/27/03
10	Seal Beams	1 day	Mon 10/27/03
11	Tape and Finish	3 days	Tue 10/28/03
12	Install FRP	2 days	Tue 10/28/03
13	Paint basement ceiling	1 day	Wed 10/29/03
14	VCT Flooring stock room	2 days	Wed 10/29/03
15	Paint	2 days	Wed 10/29/03
16	Tile delivery	0 days	Thu 10/30/03
17	Tile floor	4 days	Fri 10/31/03
18	Millwork Delivery	1 day	Thu 11/6/03
19	Millwork Installation	3 days	Fri 11/7/03
20	Finish Electric	3 days	Thu 11/6/03
21	Finish Plumbing	5 days	Mon 11/10/03
22	Wallpaper	3 days	Wed 11/12/03
23	Caulk	0 days	Fri 11/14/03
24	Final Clean up	1 day	Mon 11/17/03
25	Health Dept Inspection	1 day	Tue 11/18/03
26	Building Department Insp.	1 day	Wed 11/19/03
27	Final Turn Over	1 day	Thu 11/20/03

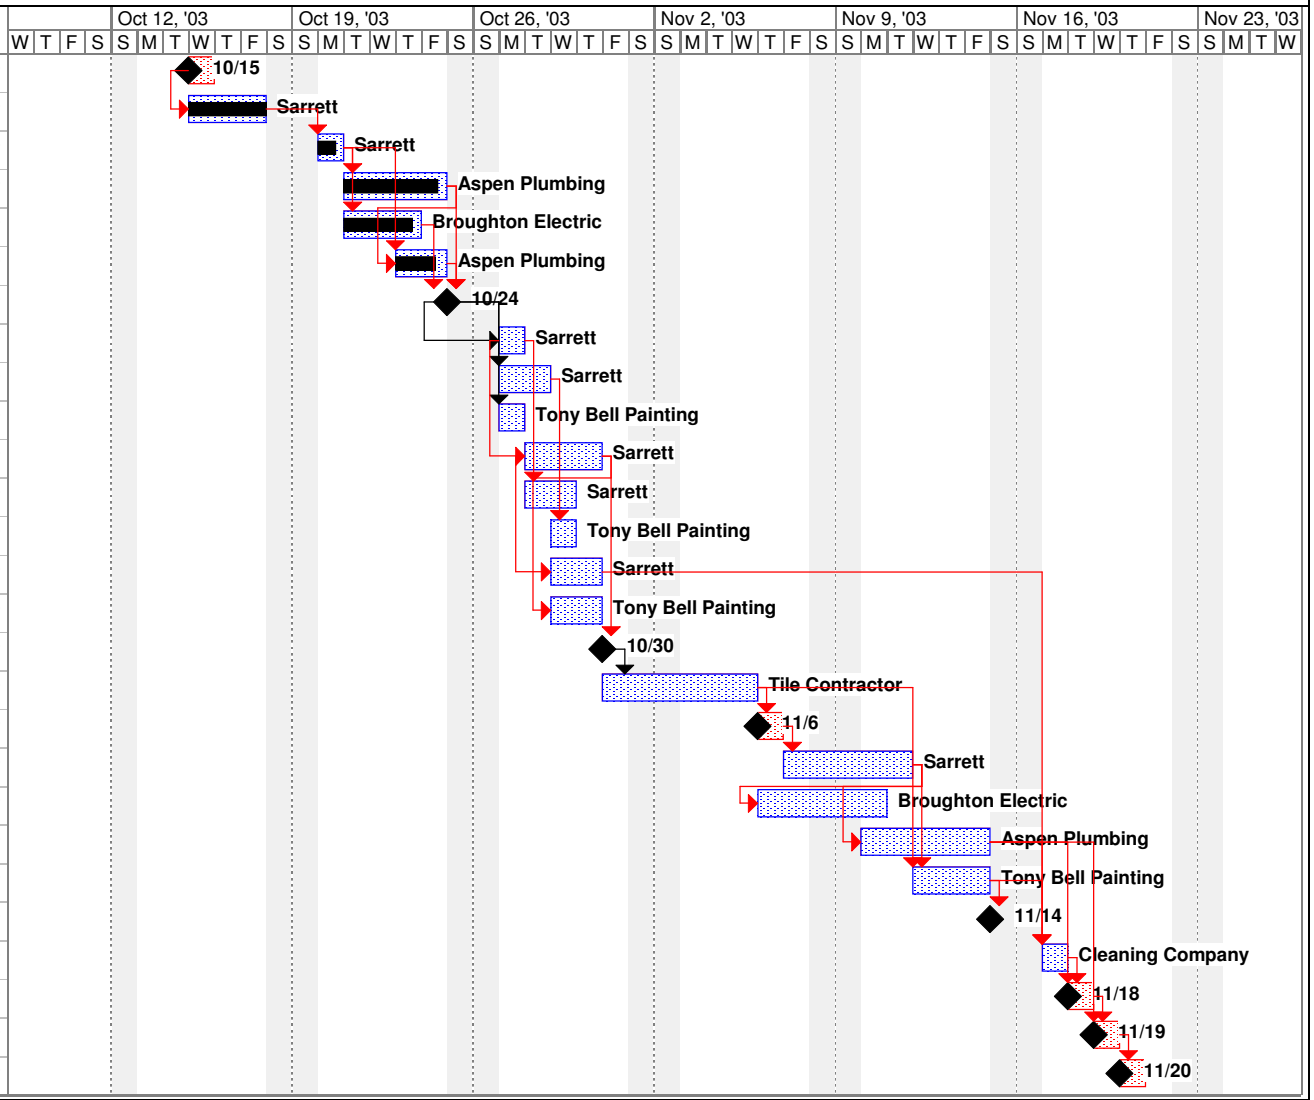

Project: RMC-Aspen - 3-02
Date: Tue 5/31/11

critical path
Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline
